


RIC Construction Update

REVISED: April 23, 2025

Active projects:

➔ Taxiway Charlie-Echo Relocation



RICHMOND
INTERNATIONAL AIRPORT



Taxiway Charlie-Echo Relocation -Project Scope



- Construction of two new stub taxiways east of the existing Concourse B apron between Taxiways A and Runway 2-20, consisting of new concrete taxiway pavement, and asphalt shoulders.
- Modification of the existing storm drainage system impacted by the Taxiways C & E Intersection Relocation project.
- Installation of taxiway centerline lighting, taxiway edge lighting and airfield signage.
- Demolition of existing concrete pavement as required by the new pavement geometry.
- Demolition of existing taxiway centerline lighting, taxiway edge lighting and airfield signage as required by the new geometry.



RIC Construction Update

Taxiway Charlie-Echo Relocation

-Project Notes


TWY E and C Relocation Project April 2025

DATE	Work Hours	Work	NOTES
04/23/2025	1 day	Contractors to meet with Ops (Dereck) to determine which signs need to be covered during the construction	<ul style="list-style-type: none">✓ Continuous monitoring of projects is required.✓ Contractors are reminded to<ol style="list-style-type: none">1. Control Dust2. Equipment should have flags and light✓ Additional independent Excavating (IX) employees will need to be badged✓ Ops to provide training video for IX contractors
04/23/2025	N/A	NOTAMS issued	
04/28/2025 – 04/28/2025	1 day	Phase 3 surfaces close. Install Low Profile Barricades.	
04/28/2025 – 04/29/2025	2 days	Temporary lighting for closure	
04/28/2025 – 05/02/2025	5 days	Survey/Pothole/Erosion Control	
04/29/2025 – 04/30/2025	2 days	Sawcut demolition limits	
04/29/2025 – 05/05/2025	5 days	Antigo-Demo concrete pavement	



Taxiway Charlie-Echo Relocation

-Phase 3 drawing

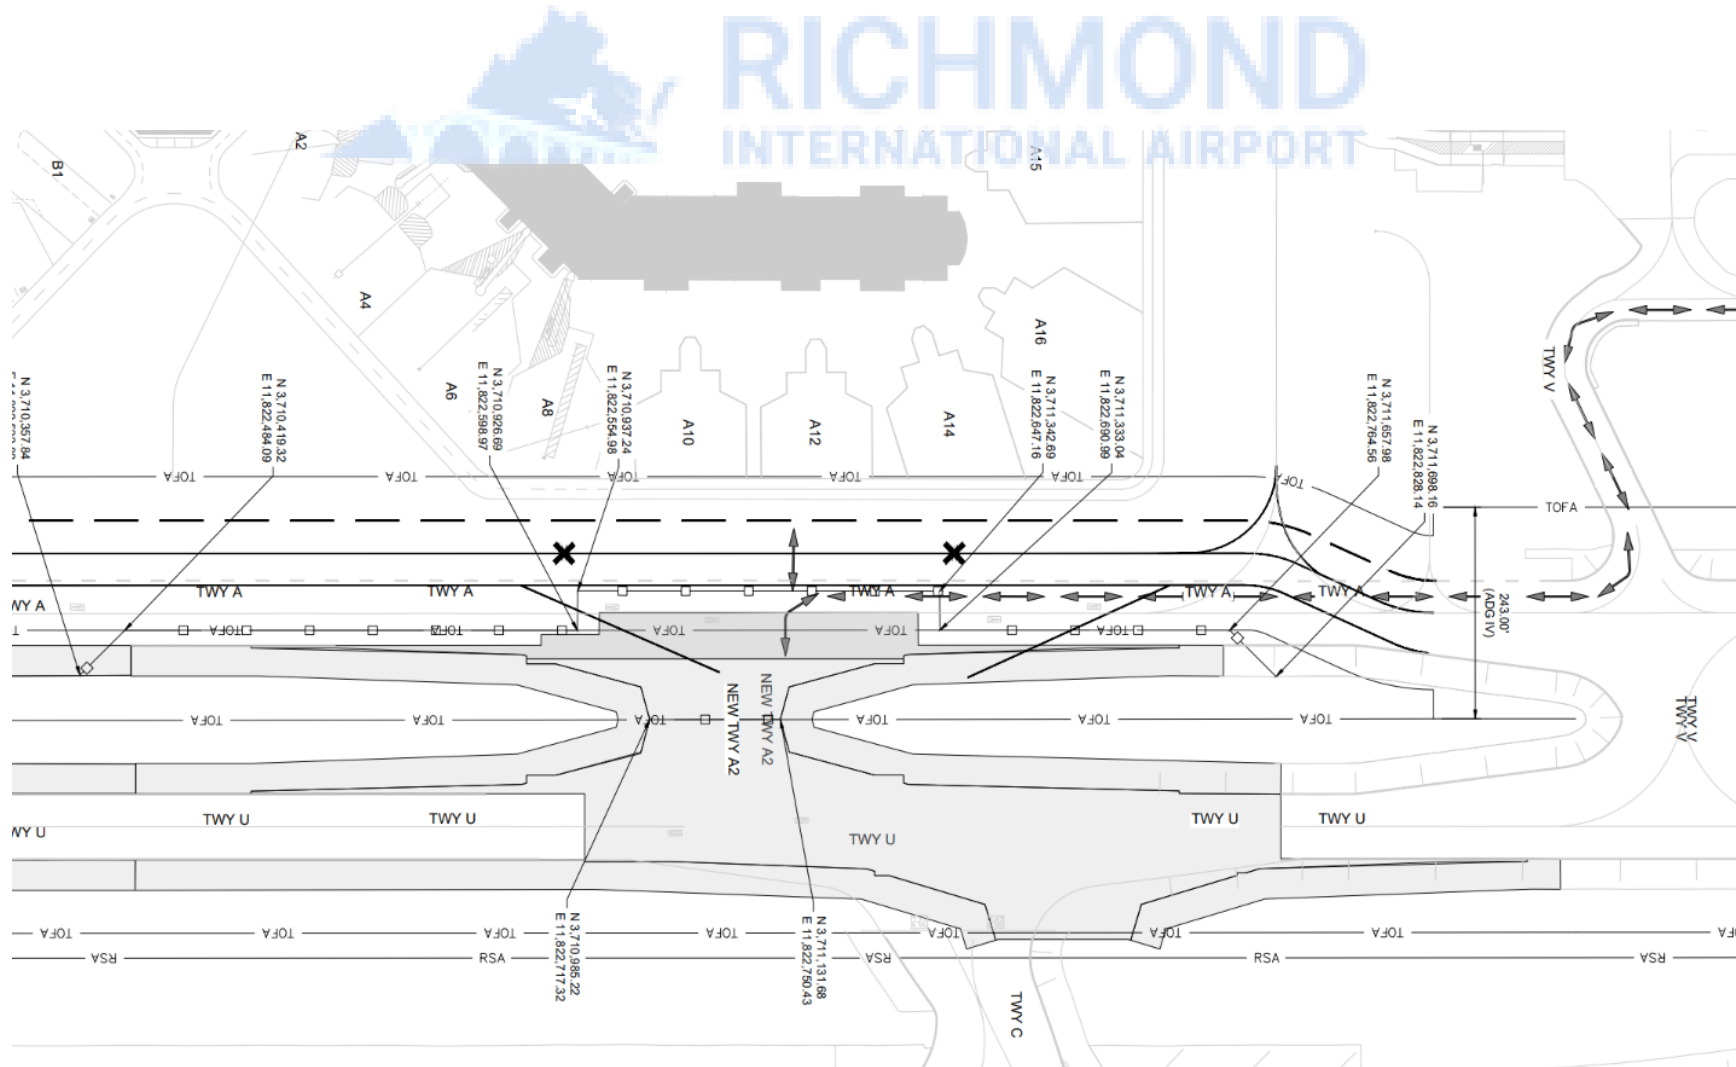

Taxiway Charlie-Echo Relocation

-Pictures



RICHMOND
INTERNATIONAL AIRPORT

